


Choptank Road Maintenance of Traffic Public Workshop



April 9, 2007

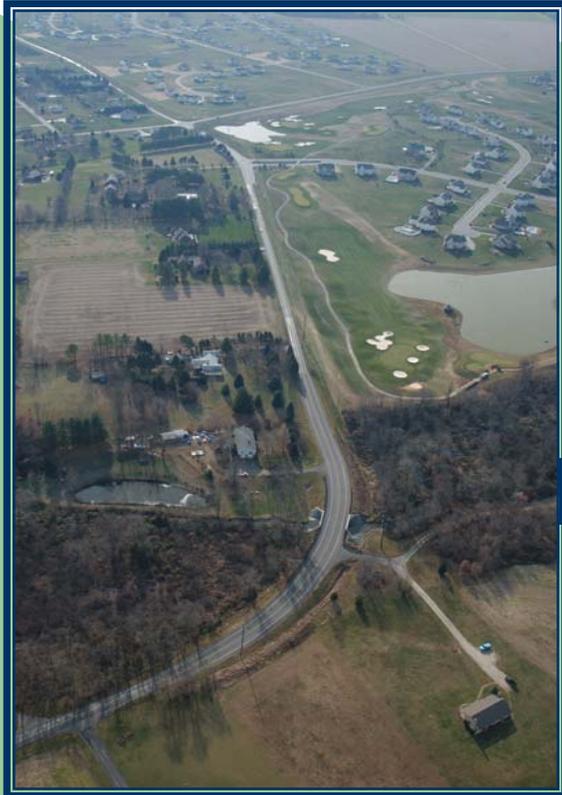

Delaware Department
of Transportation

**Edwards
Kelcey**
ENGINEERS
ARCHITECTS
PLANNERS
CONSTRUCTORS



Project Overview

- Purpose of Meeting
- Anticipated Construction Duration
 - Spring 2007 through Winter 2009
- Project Contractor
 - Greggo & Ferrara, Inc.

What's Happening now...

- Fence relocations prior to construction
- Advanced utility relocations
- Archaeology investigation at Sharp Farm




Project Phasing

- Local and emergency access to all residences will be maintained throughout construction
- School bus service and mail delivery service will remain uninterrupted during construction
- To have any concerns addressed during construction, please contact DeIDOT Public Relations



Delaware Department
of Transportation

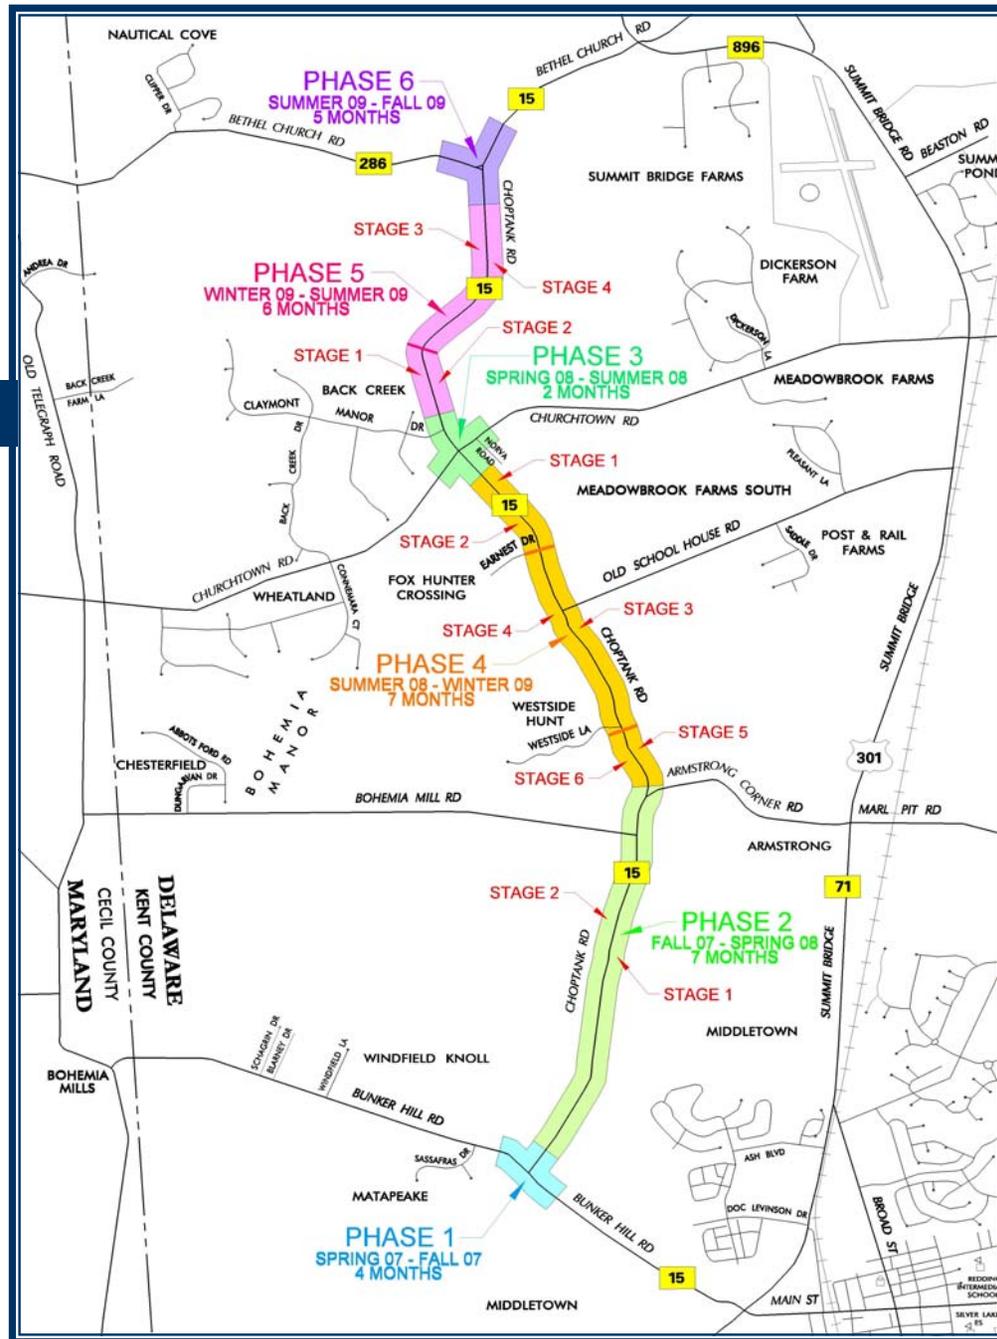

Phase 1 - Construction

Limits:

Bunker Hill Road at Choptank Road
Appoquinimink School Drive

Anticipated Construction Duration:

Spring 2007 to Fall 2007 – 4 months


Major Construction Tasks:

- Appoquinimink School Drive
- Bunker Hill Road/Choptank Road Reconstruction
- Roundabout
- Stormwater Management Facilities

Phase 1 - Traffic & Detour

Stages 2 & 3

- Existing traffic patterns will remain for Stage 1
- Approximate 4-month duration
- No through traffic permitted on Bunker Hill Rd.
- No access to/from Choptank Rd. at Bunker Hill Rd.
- Local traffic only permitted on Bunker Hill Rd. east of Sassafra Dr.

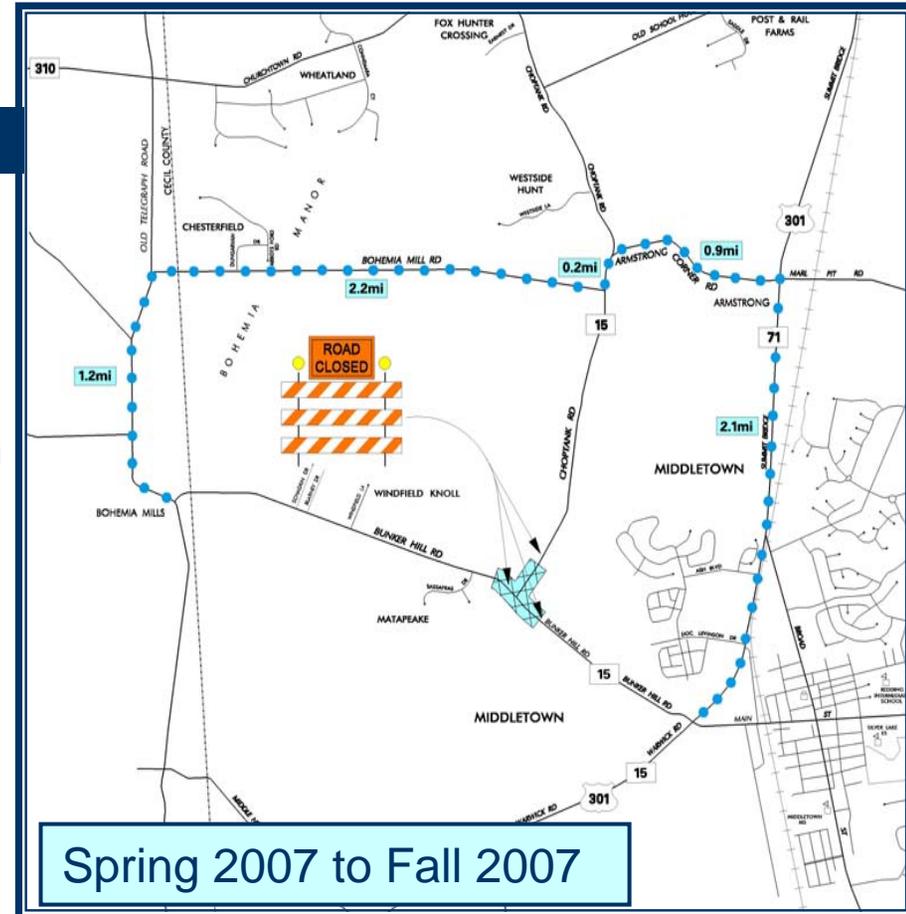

Phase 1 - Traffic & Detour

Stages 2 & 3



Typical Project Local Traffic Only signage



Typical Project Total Road Closure signage



Phase 2 - Construction

Limits:

Choptank Road – Bunker Hill Road to Armstrong Corner Road

Anticipated Construction Duration:

Fall 2007 to Spring 2008 – 7 months

Major Construction Tasks:

- Choptank Road Reconstruction
- Stormwater Management Pond
- Roadway Drainage Facilities
- Intersection Reconstruction
 - Bohemia Mill Road
 - Armstrong Corner Road




Delaware Department
of Transportation



Phase 2 - Traffic & Detour All Stages

- Approximate 7-month duration
- Two-lanes permitted at all times on Choptank Rd. between Bohemia Mill Rd. and Armstrong Corner Rd.
- No through traffic permitted on Choptank Rd. at Bunker Hill Rd.
- Local traffic only permitted on Choptank Rd. south of Bohemia Mill Rd.

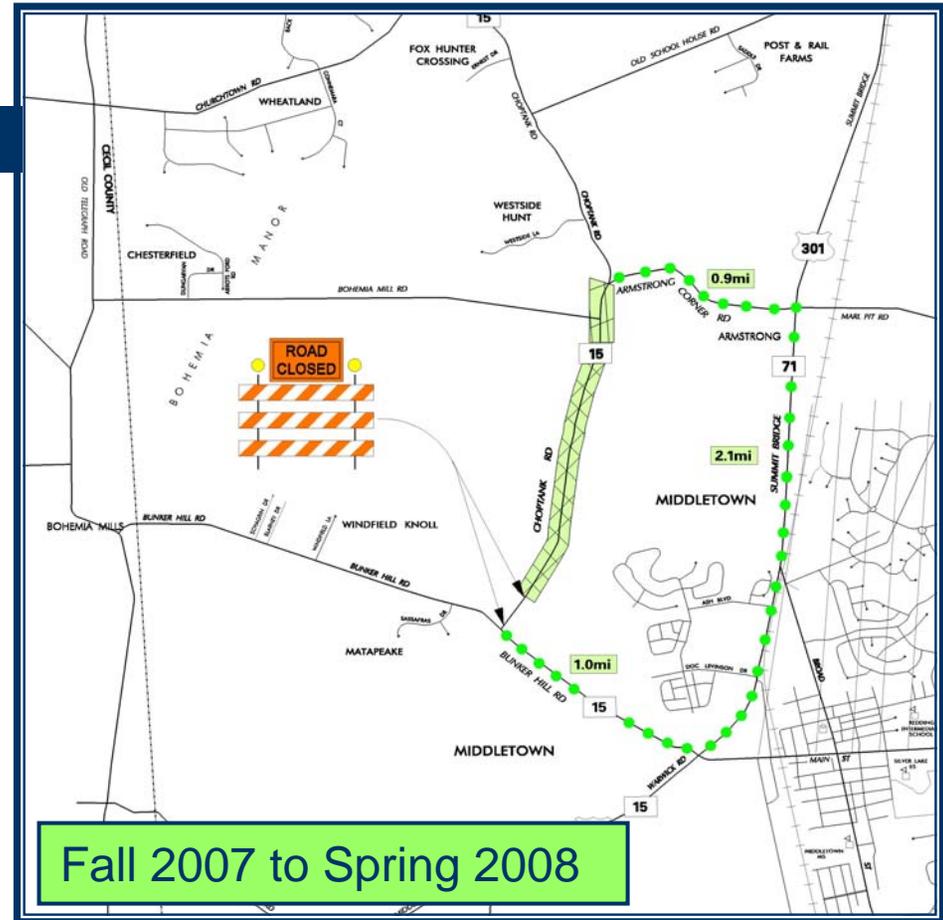

Phase 3 - Construction

Limits:

Churchtown Road

Choptank Road - Churchtown Road to Clayton Manor Drive

Anticipated Construction Duration:

Spring 2008 to Summer 2008 – 2 months

Major Construction Tasks:

- Churchtown Road/Choptank Road Reconstruction
- Roundabout
- Roadway Drainage Facilities
- Intersection Reconstruction
 - Clayton Manor Drive




Delaware Department
of Transportation



Phase 3 - Traffic & Detour

All Stages

- Approximate 2-month duration
- No through traffic permitted on Choptank Rd. and Churchtown Rd.
- Only one access for Back Creek Development & Golf Course will be allowed at Back Creek Dr. and Churchtown Rd.

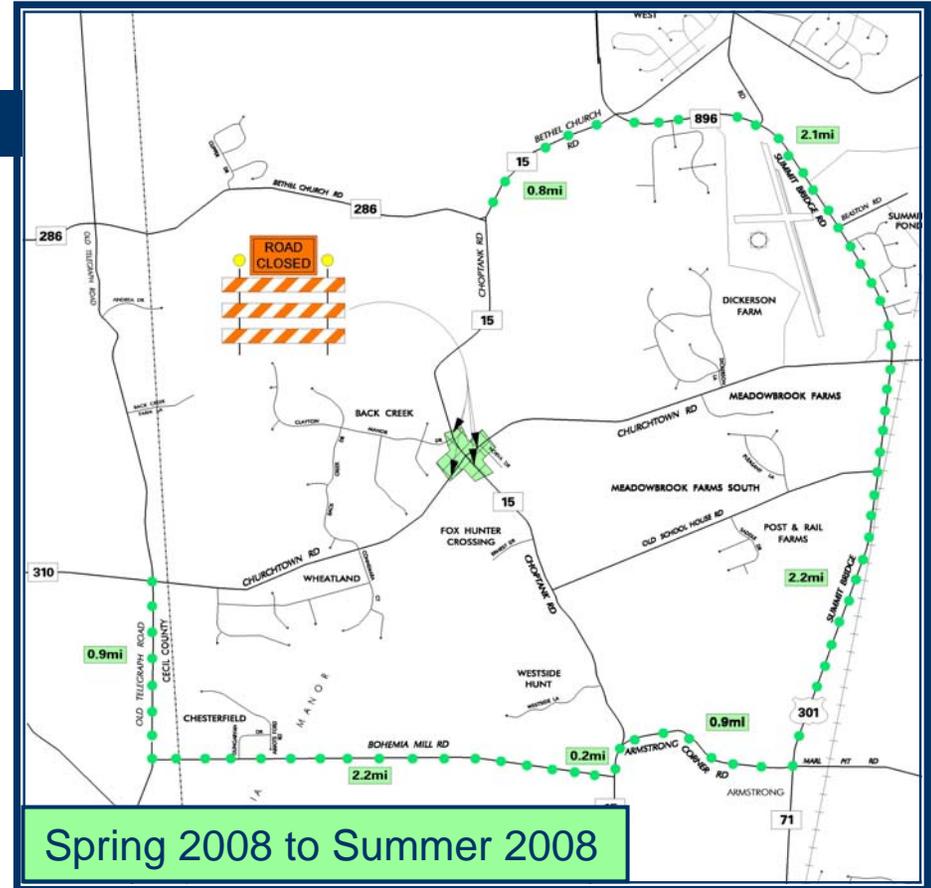

Phase 4 - Construction

Limits:

Choptank Road – Armstrong Corner Road to Churchtown Road

Anticipated Construction Duration:

Summer 2008 to Winter 2009 – 7 months


Major Construction Tasks:

- Choptank Road Reconstruction
- Old School House Road drainage pipe
- Intersection Reconstruction
 - Westside Lane (access to Westside Hunt Development)
 - Old School House Road
 - Ernest Drive (access to Fox Hunter Crossing Development)

Phase 4 - Traffic & Detour

Stages 1 & 2


- Approximate 2-month duration
- No through traffic permitted on Choptank Rd. at Ernest Dr.
- Local traffic only permitted on Choptank Rd. south of Churchtown Rd.
- Only one access to the Fox Hunter Crossing Development permitted at Colonel Clayton Dr. and Churchtown Rd.

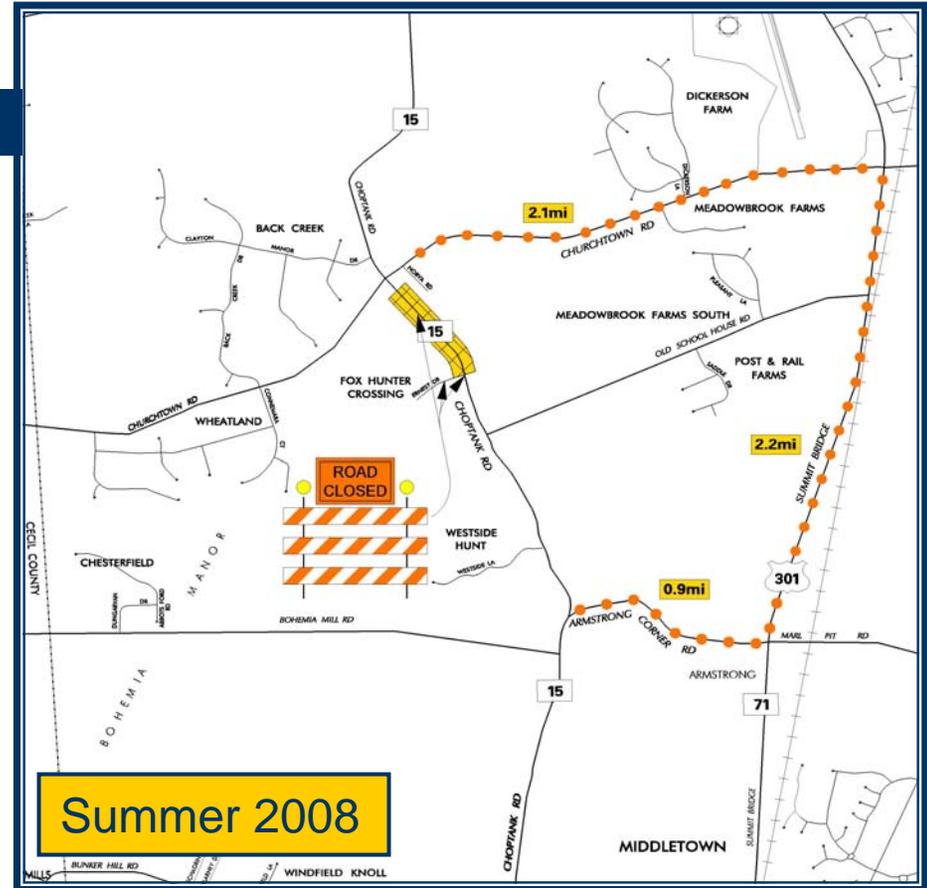

Phase 4 - Traffic & Detour

Stages 3, 4 & 5


- Approximate 3-month duration
- No through traffic permitted on Choptank Rd. at Ernest Dr.
- No through traffic permitted on Old School House Rd. during Stage 3
- Local traffic only permitted on Choptank Rd. north of Westside Ln.
- Fox Hunter Crossing entrance at Ernest Dr. re-opened (left-turn out and right-turn in only)

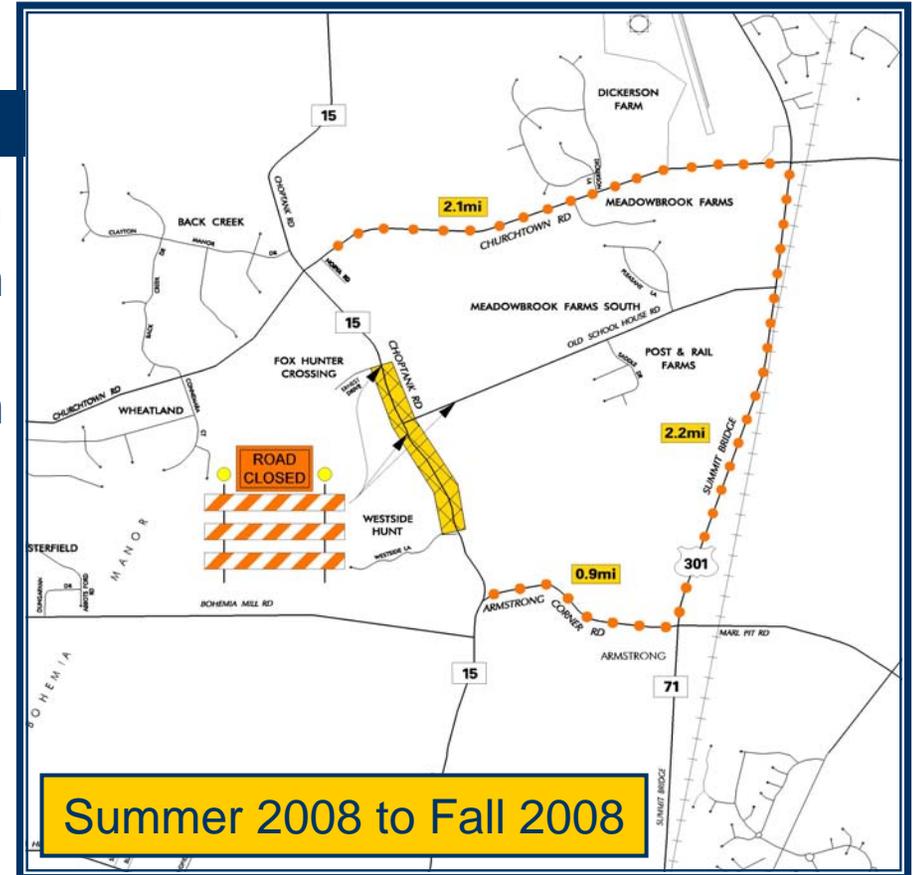

Phase 4 - Traffic & Detour

Stages 6 & 7

- Approximate 2-month duration
- No through traffic permitted on Choptank Rd. at Westside Ln.
- Local traffic only permitted on Choptank Rd. north of Armstrong Corner Rd.
- Access to Westside Hunt Development permitted (left-turn out and right-turn in only)

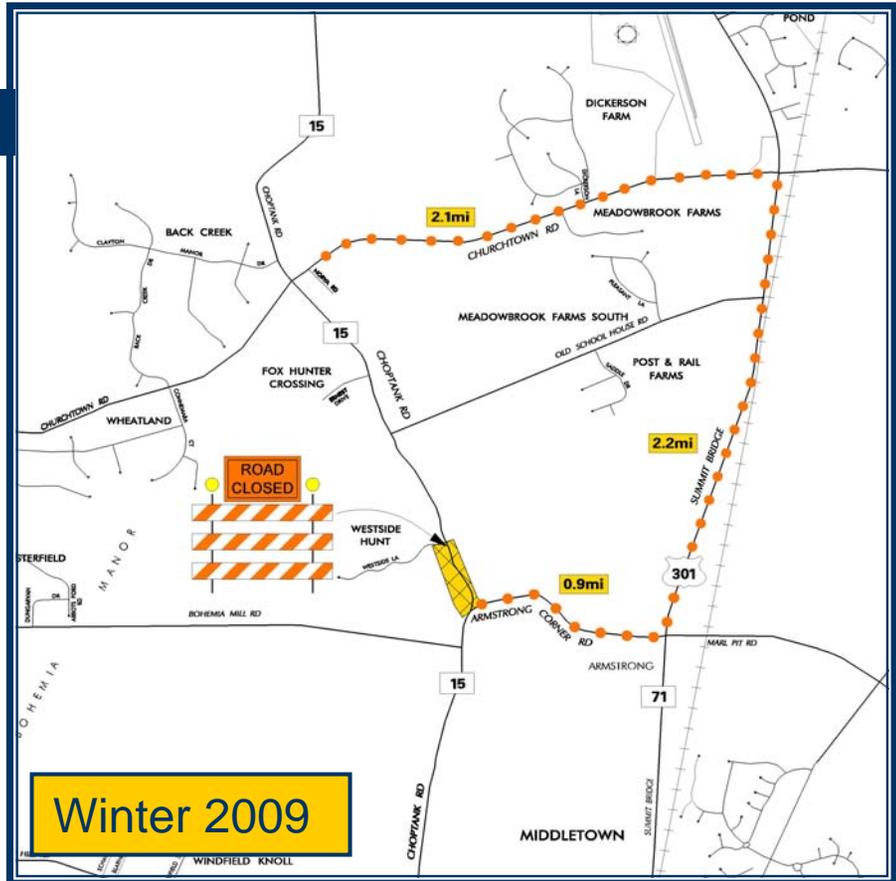

Phase 5 - Construction

Limits:

Choptank Road – Clayton Manor Drive to Bethel Church Road

Anticipated Construction Duration:

Winter 2009 to Summer 2009 – 6 months


Major Construction Tasks:

- Choptank Road Reconstruction
- Roadway Drainage Facilities
- Back Creek Bridge milling and resurfacing
- Guardrail Improvements at Back Creek Bridge

Phase 5 - Traffic & Detour

All Stages

- Approximate 6-month duration
- No through traffic permitted on Choptank Rd. at the Back Creek Bridge
- Local traffic only permitted on Choptank Rd. south of Bethel Church Rd. and north of Clayton Manor Dr.

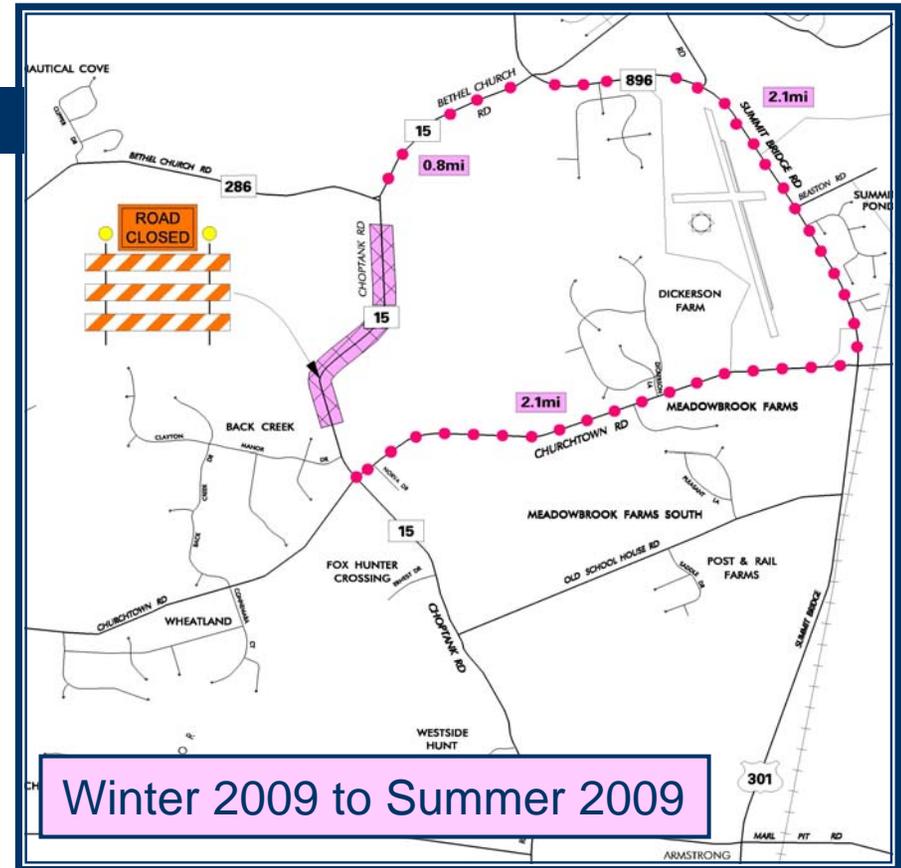

Phase 6 - Construction

Limits:

Bethel Church Road at Choptank Road

Anticipated Duration:

Summer 2009 to Winter 2009 – 5 months

Major Construction Tasks:

- Bethel Church Road/Choptank Road Reconstruction
- Roundabout
- Roadway Drainage Facilities

Phase 6 – Traffic All Stages

- No Detour utilized for this Phase of construction.
- Two lanes of traffic will be maintained at all times in all directions with the provision of temporary lane closures.
- Flaggers will be utilized for temporary lane closures.
