

BIKEWAY PROJECT UPDATES

Contract No. T201330012; Junction & Breakwater Pathway - Rehoboth Beach Extension

Project Schedule (Subject to change)


- Final Right of Way is scheduled for May 27, 2020
- Final Construction is scheduled for August 15, 2020
- PS&E Submittal is scheduled for November 3, 2020

Project Description

Constructing a two-way cycle track from Canal Crossing Blvd. to the Rehoboth Canal Bridge. The cycle track is to be constructed behind the existing motel in which right-of-way will need to be acquired. The cycle track will be along the north side of Rehoboth Blvd and tie into the existing bridge.

Project Notes

The semi-final plans were submitted, and comments returned in February 2020.

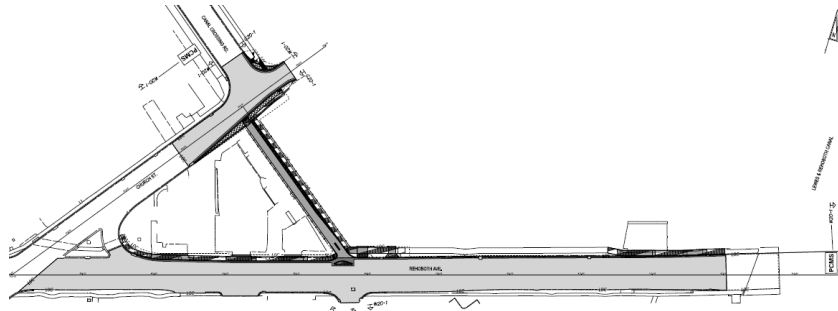

Contract No. T201930001; Georgetown to Lewes Trail Phase 8

Project Schedule (Subject to change)

- Final ROW is scheduled for March 2020
- Final Construction is scheduled for March 2020
- PS&E is scheduled for June 2020

Project Description

Constructing a 10' wide shared-use path from the Georgetown Little League Park to Airport Road. The path will be on the north side of the existing active railroad line.

Project Notes

The preliminary plans were submitted, and comments returned in January 2020.



Contract No. T202030001; Georgetown to Lewes Trail, Cool Spring Road to Fisher Road

Project Schedule (Subject to change)


- Preliminary Plans are scheduled for June 2020
- Semi-final Construction and Right-of-Way Submittal is scheduled for October 2020
- Final Right-of-Way Plan Submittal is scheduled for February 2021
- Final Construction Submittal is scheduled for February 2021
- PS&E Submittal is scheduled for April 2021

Project Description

Constructing a 10' wide shared-use path from Cool Spring Road to the intersection of Fisher Road. The path is anticipated being on the north side of SR9.

Project Notes

The survey plans were submitted, and comments returned in May 2020.

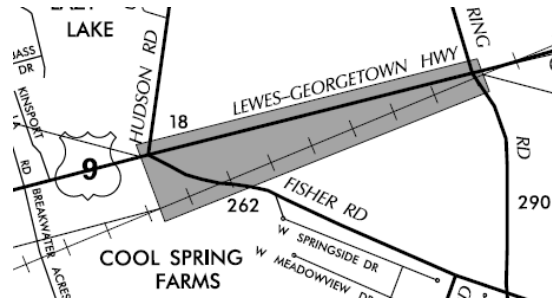


Georgetown to Lewes – Log Cabin Hill Road to Cool Spring Road

Project Schedule

- Began Construction in April 2020
- **Project completed by June 2020**

Project Description

Constructing a 10' wide shared-use path from the end of the existing path at Log Cabin Hill Road to Cool Spring Road. The path will connect at Cool Spring Road and not tie into the existing shoulder along Route 9.

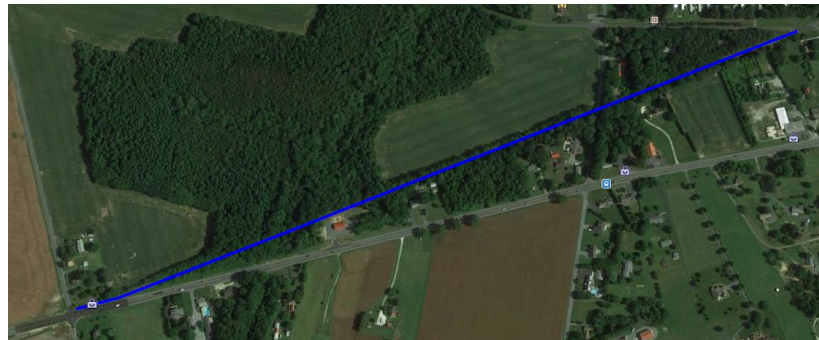

Contract No. T201801501; Delaware Avenue

Project Schedule (Subject to change)


- Final right-of-way anticipated for February 2020.
- PS&E is scheduled for December 2020.

Project Description

Constructing a two-way cycle track from SR896 to Library Avenue.

Project Notes

The final plans were submitted in October 2019. DelDOT is coordinating with the developer of College Square Redevelopment to provide bike facilities across Library Ave to and from the Delaware Ave bikeways project. An 8' wide SUP's are proposed on each side of the site entrance of College Square. As per a Skype meeting on April 9th, the proposed connection from the Bikeway Project to College Square is through modified islands on the east side of the Library Avenue/Delaware Avenue/College Square signalized intersection. Additional improvements requested from College Square are: 1) Extending the 8' wide path through the ADA ramp on the NE Corner; 2) Adjusting the location of the proposed entrance monument on the NE Corner; Moving the existing light pole on the College Square property to accommodate 1 and 2.

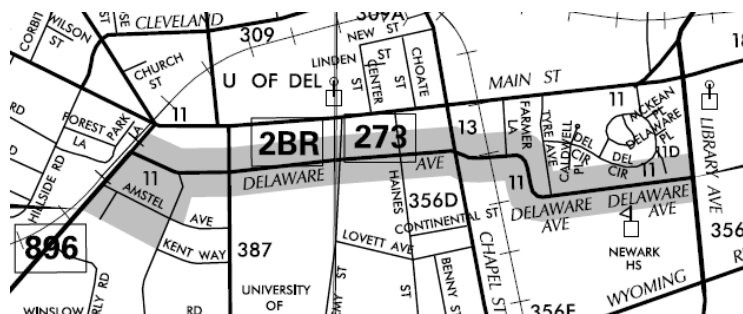

Contract No. T201701202; Capital City Trail Phase II, Gateway Center to South State Street

Project Schedule (Subject to change)

- Began Construction - April 2020
- End Construction - July 2020

Project Description

Construct a 10' wide shared-use path on the south side of SR10 from the Gateway Shopping Center to South State Street.

Contract No. T201701301; Milton Rail to Trail – Phase 2

Project Schedule (Subject to change)

- Currently under construction
- **Project completed by June 2020**

Project Description

Constructing a 10' wide shared-use path from Federal Street to Lavinia Street in Milton.

Project Notes

Details for a virtual ribbon cutting ceremony are being worked out. The Council will be notified once finalized. This will be the first type of ceremony conducted by DelDOT.

Contract No. T201830001; Capital City Trail Phase III, South State Street to US13

Project Schedule (Subject to change)


- Semi-Final is scheduled for September 2020
- Final ROW is scheduled for February 2021
- Final Construction is scheduled for February 2021
- PS&E is scheduled for May 2021

Project Description

Construct a 10' wide shared-use path on the south side of SR10 from South State Street to 0.35-miles west at First Tenth Court, tying into the improvements of the East Camden Bypass project (T201709503).

Project Notes

The preliminary plans were submitted and comments due in June 2020.

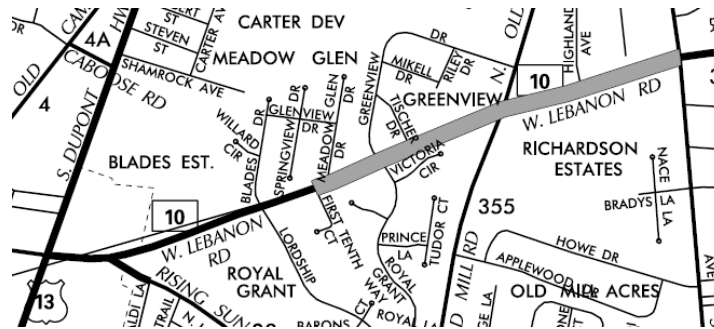

Contract No. T201630003; Senator Bikeway Phase I Saulsbury Road to Washington Street

Project Description

Constructed a two-way cycle track from Weston Drive to Cecil Street and on-road facilities to Washington Street.

Project Notes

During and after construction, issues developed with Bennie Smith Funeral Home. Although there is no parking permitted within the cycle track, Mr. Smith could have a hearse parked there during funeral services only. On many occasions there are multiple vehicles parked in the cycle track when there is a funeral service and when not. DelDOT and the City of Dover met with the Smith's in early March where a compromise could not be reached. At this time no further meetings are being scheduled with the funeral home. The existing No Parking signs will be revised to indicate "Hearse permitted during funeral service only". Signs have been installed by DelDOT.



Georgetown to Lewes Trail – Sign Installation

Project Description

Install audible warning signs along existing Georgetown to Lewes Trail.

Project Notes

To address public concerns of both runners and bicyclists not giving adequate warning when passing, DelDOT will be installing audible warning signs along the path. The signs have already been fabricated and anticipate being installed before Memorial Day weekend. A “thank you” needs to go out to Mike Krumrine who helped make these signs for DelDOT.



2020 Bike Month Events

May 6th – Legislators Bike Ride

May 13th – DelDOT/Dover Bike to Work Day

May 15th - Newark, Wilmington and Lewes Bike to Work Day

Due to the COVID-19 pandemic, Bike Month events in May have been cancelled. The League of American Bicyclists has postponed the promotion of Bike to Work Week until September 21-27, 2020, with Bike to Work Day coinciding with Car Free Day on September 22, 2020. Many of these events are anticipated being rescheduled until September but do not have any details at this time.

