CHANGEABLE MESSAGE BOARDS

PRIOR TO DETOUR
(10 Days prior to beginning of detour)

CMS-1

SYCAMORE ROAD CLOSED	STARTING ON XX/XX/XX

DURING DETOUR

CMS-1

SYCAMORE ROAD CLOSED	FOLLOW POSTED DETOUR

PRIOR TO DETOUR
(10 Days prior to beginning of detour)

CMS-2

XXXXXXXX XXXXXXXX XXXXXXXX	XXXXXXXX XXXXXXXX XXXXXXXX

DURING DETOUR

CMS-2

XXXXXXXX XXXXXXXX XXXXXXXX	XXXXXXXX XXXXXXXX XXXXXXXX

SPECIAL SIGNS

U

48"

72"

Sycamore Rd CLOSED at E.Elliots Dam Road	6"C 6"C 6"C 6"C
FOLLOW DETOUR	6"C 6"C

D/G ORANGE

BLACK LEGEND

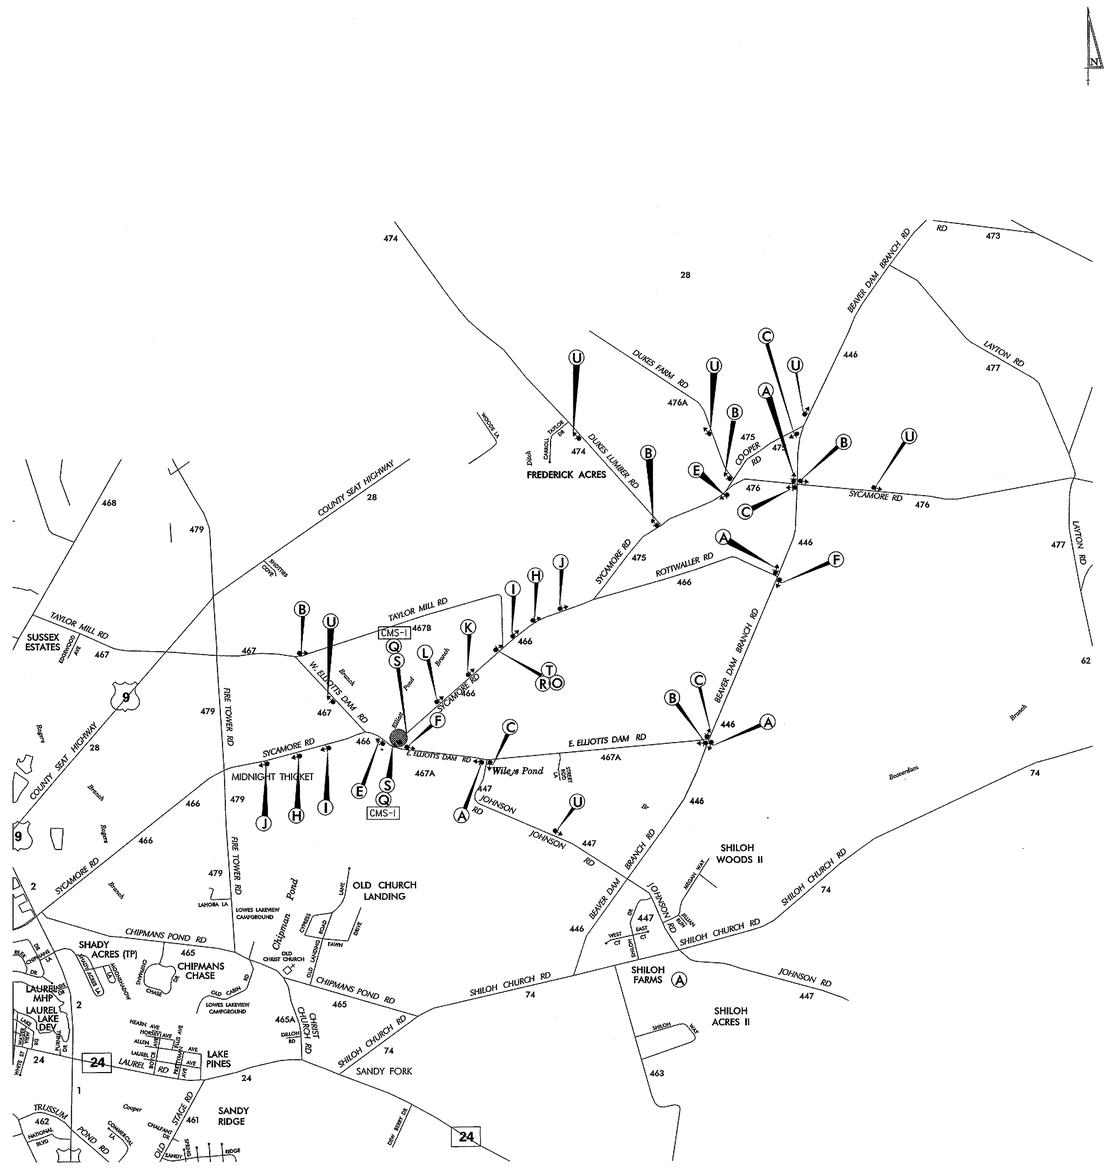

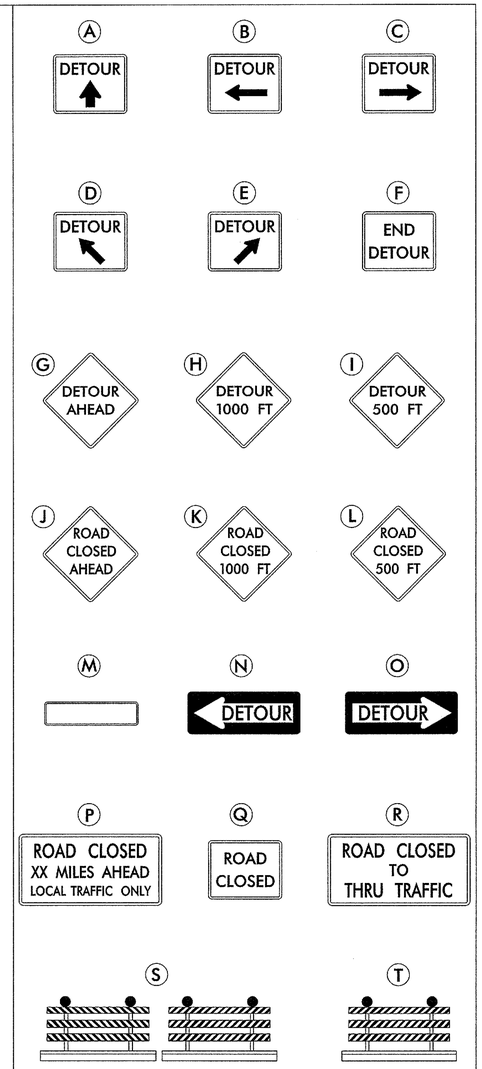

GENERAL NOTES

1. ALL DETOUR SIGNING INCLUDING, TRAILBLAZERS, ARE TO BE SUPPLIED AND MAINTAINED BY THE GENERAL CONTRACTOR IN COMPLIANCE TO THE DE MANUAL OF UNIFORM TRAFFIC CONTROL DEVICES.
2. THE CONTRACTOR SHALL COMPLY WITH GUIDELINES IN "THE DELAWARE MANUAL ON UNIFORM TRAFFIC CONTROL DEVICES (DE- MUTCD PART 6) FOR LIGHTS, BARRICADES AND SIGNS.(AS PER LATEST REVISION)
3. FIELD CONDITIONS MAY DICTATE CHANGES AT SOME TIME DURING THE LIFE OF THE CONTRACT. IN THE EVENT OF OMISSIONS OR CORRECTIONS, THE SIGNING PROVISIONS OF THE DELAWARE MANUAL ON UNIFORM TRAFFIC CONTROL DEVICES WILL PREVAIL.
4. SIGNS J THROUGH L AND P THROUGH R ,THE WORD (ROAD) SHOULD BE CHANGED TO RAMP, R/R OR BRIDGE WHERE APPLICABLE.
5. WARNING SIGNS SHOULD BE MOUNTED ON BREAKAWAY POSTS AND HAVE RETROREFLECTIVE FLUORESCENT SHEETING.
6. "S" BARRICADES SHALL COMPLETELY RUN THE FULL WIDTH OF ROADWAY.
7. BARRICADES SHALL BE A MINIMUM OF 6 FEET WIDE UNLESS DIRECTED BY THE ENGINEER.

RECOMMENDED _____ DATE: _____ | RECOMMENDED _____ DATE: _____ | RECOMMENDED _____ DATE: _____ | APPROVED CHIEF SAFETY OFFICER _____ DATE: _____ | APPROVED TRAFFIC ENGINEER _____ DATE: _____

DELAWARE DEPARTMENT OF TRANSPORTATION

ADDENDUM / REVISIONS

NOT TO SCALE

BR 3-368 ON SYCAMORE ROAD OVER ELLIOT POND BRANCH

CONTRACT	ROAD NO.	466
T201107306	DESIGNED BY:	MF
COUNTY	CHECKED BY:	
SUSSEX		

DETOUR PLAN

SHEET NO.	TOTAL SHTS.
1	1
